ID		Task Mode	Task Name	Duration	Start	Finish	Predeces	Resource Names
1			Research and analysis- phase 1	40 days	Mon 14/01/19	Fri 08/03/19		
2			Research and analysis - phase 2	70 days	Mon 11/03/19	Fri 14/06/19	1	
3			Review current IRMP	40 days	Mon 14/01/19	Fri 08/03/19		
4			Review of 2020	20 days	Mon 14/01/19	Fri 08/02/19		
5			Initial stakeholder engagement	70 days	Mon 11/03/19	Fri 14/06/19	1,3,4	
6			Develop specific proposals for change	50 days	Mon 17/06/19	Fri 23/08/19	2	
7			Consultation 2 preparation	20 days	Mon 26/08/19	Fri 20/09/19	6	
8			Consultation 2	60 days	Mon 23/09/19	Fri 13/12/19	7	
9			Consider Consultation 2 results	20 days	Mon 16/12/19	Fri 10/01/20	8	
10			Outcome of Fire Cover Review Known	1 day	Mon 13/01/20	Mon 13/01/20	9	
11			Implementation planning	100 days	Mon 13/01/20	Fri 29/05/20	9	
12			Publish IRMP	20 days	Mon 01/06/20	Fri 26/06/20	9,11	
13			Delivery start date	1 day	Mon 29/06/20	Mon 29/06/2	11,12	

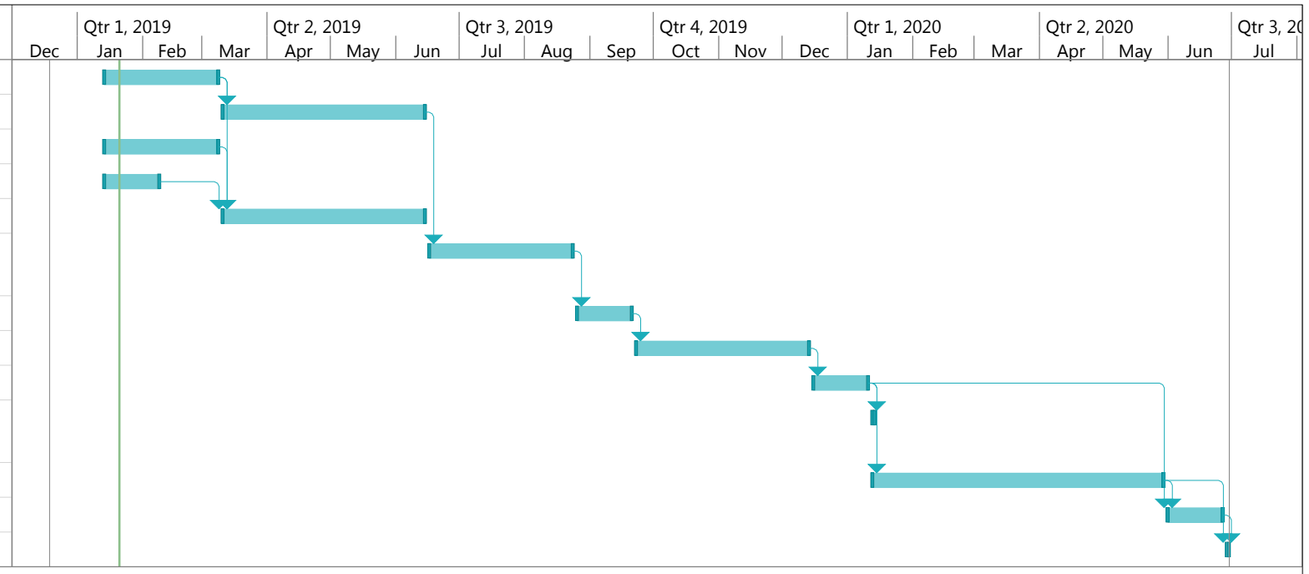

Project: FireCover plan V2.1
Date: Mon 21/01/19

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
